

PRO-MATRIX

PRECISION IN EVERY ESTIMATE

ITEM #	REV. SHEET	DETAIL	CSI SECT	Sub Contractor	DESCRIPTION	QTY.	WASTAGE	QTY W/ST WASTAGE	UNIT	UNIT PRICE	TOTAL LABOR HOURS	PER HOUR LABOR RATE	TOTAL LABOR COST	UNIT MATERIAL COST	TOTAL MATERIAL COST	ITEM COST	TRADE COST	UNIT ITEM COST WITH MARKUPS	TOTAL ITEM COST WITH MARKUPS
CLICK HERE TO GO BACK TO COST SUMMARY																			
Sub-Total (\$ 36,679,843)					Date: 4/5/23														
Material Sales Tax 4.250% 1,588,203 (Adjust the percentage for Material tax as required)					Project: Westhill High School														
Overhead & Profit / Material (Overhead) 10% 1,713,287 (Adjust the percentage for Overhead & Profit as required)					Project Location: 125 Roxbury Road Stamford, CT, 06902														
Overhead & Profit (Labor) 10% 1,958,080 (Adjust the percentage for Overhead & Profit as required)					Project and Wage Type: Open Shop/Non Union														
BIDD Fee 0.31% 821,466 (Adjust the percentage for BIDD Fee as required)																			
TOTAL BID (\$ 42,052,504)																			
Material Wastage 1 0% (For Quantities in EACH & L/S)					Gross Internal Area of Structure (SF) _____														
Material Wastage 2 5% (For Quantities in L/S, SF, AC, CY, LB, TONS)					Covered Area of Structure (SF) _____														
(Changing the wastage percentage here will update the wastage for whole lot)					No. of Units _____														
					No. of Floors and Overall Height/ft _____														
					Handicapping Area (SF) _____														
					Soft scaping Area (SF) _____														
To change hourly rates for any trade please go to "Hourly Rates" Tab																			

1				General Requirements	Design and Permitting	1		1	1										
2				General Requirements	Architectural By Owner	1		1	1										
3				General Requirements	Engineering (Assumed By Owner)	1		1	1										
4				General Requirements	Surveying	1		1	1										
5				General Requirements	Soils Report (Assumed By Owner)	1		1	1										
6				General Requirements	Geological Report (Assumed By Owner)	1		1	1										
7				General Requirements	Concrete Testing	1		1	1										
8				General Requirements	Permit Fee (Based on Interior Finish Area)	1		1	1										
9				General Requirements	Permit Fee (Based on Interior Finish Area)	1		1	1										
10				General Requirements	Permit Fee (Based on Interior Finish Area)	1		1	1										
11				General Requirements	Permit Fee (Based on Interior Finish Area)	1		1	1										
12				General Requirements	Utilities During Construction (Based on Interior Finish Area)	1		1	1										
13				General Requirements	Part-5 Permit (Based on Interior Finish Area)	1		1	1										
14				General Requirements	Temporary Power (Based on Interior Finish Area)	1		1	1										
15				General Requirements	Equipment and Tools	1		1	1										
16				General Requirements	Tool Shed	1		1	1										
17				General Requirements	Tool Shed	1		1	1										
18				General Requirements	Tool Shed	1		1	1										
19				General Requirements	Tool Shed	1		1	1										
20				General Requirements	Tool Shed	1		1	1										
21				General Requirements	Tool Shed	1		1	1										
22				General Requirements	Tool Shed	1		1	1										
23				General Requirements	Tool Shed	1		1	1										
24				General Requirements	Tool Shed	1		1	1										
25				General Requirements	Tool Shed	1		1	1										
26				General Requirements	Tool Shed	1		1	1										
27				General Requirements	Tool Shed	1		1	1										
28				General Requirements	Tool Shed	1		1	1										
29				General Requirements	Tool Shed	1		1	1										
30				General Requirements	Tool Shed	1		1	1										
31				General Requirements	Tool Shed	1		1	1										
32				General Requirements	Tool Shed	1		1	1										
33				General Requirements	Tool Shed	1		1	1										
34				General Requirements	Tool Shed	1		1	1										
35				General Requirements	Tool Shed	1		1	1										
36				General Requirements	Tool Shed	1		1	1										
37				General Requirements	Tool Shed	1		1	1										
38				General Requirements	Tool Shed	1		1	1										
39				General Requirements	Tool Shed	1		1	1										
40				General Requirements	Tool Shed	1		1	1										
41				General Requirements	Tool Shed	1		1	1										
42				General Requirements	Tool Shed	1		1	1										
43				General Requirements	Tool Shed	1		1	1										
44				General Requirements	Tool Shed	1		1	1										
45				General Requirements	Tool Shed	1		1	1										
46				General Requirements	Tool Shed	1		1	1										
47				General Requirements	Tool Shed	1		1	1										
48				General Requirements	Tool Shed	1		1	1										
49				General Requirements	Tool Shed	1		1	1										
50				General Requirements	Tool Shed	1		1	1										
51				General Requirements	Tool Shed	1		1	1										
52				General Requirements	Tool Shed	1		1	1										
53				General Requirements	Tool Shed	1		1	1										
54				General Requirements	Tool Shed	1		1	1										
55				General Requirements	Tool Shed	1		1	1										
56				General Requirements	Tool Shed	1		1	1										
57				General Requirements	Tool Shed	1		1	1										
58				General Requirements	Tool Shed	1		1	1										
59				General Requirements	Tool Shed	1		1	1										
60				General Requirements	Tool Shed	1		1	1										
61				General Requirements	Tool Shed	1		1	1										
62				General Requirements	Tool Shed	1		1	1										
63				General Requirements	Tool Shed	1		1	1										
64				General Requirements	Tool Shed	1		1	1										
65				General Requirements	Tool Shed	1		1	1										
66				General Requirements	Tool Shed	1		1	1										
67				General Requirements	Tool Shed	1		1	1										
68				General Requirements	Tool Shed	1		1	1										
69				General Requirements	Tool Shed	1		1	1										
70				General Requirements	Tool Shed	1		1	1										
71				General Requirements	Tool Shed	1		1	1										
72				General Requirements	Tool Shed	1		1	1										
73				General Requirements	Tool Shed	1		1	1										
74				General Requirements	Tool Shed	1		1	1										
75				General Requirements	Tool Shed	1		1	1										
76				General Requirements	Tool Shed	1		1	1										
77				General Requirements	Tool Shed	1		1	1										
78				General Requirements	Tool Shed	1		1	1										
79				General Requirements	Tool Shed	1		1	1										
80				General Requirements	Tool Shed	1		1	1										
81				General Requirements	Tool Shed	1		1	1										
82				General Requirements	Tool Shed	1		1	1										
83				General Requirements	Tool Shed	1		1	1										
84				General Requirements	Tool Shed	1		1	1										
85				General Requirements	Tool Shed	1		1	1										
86				General Requirements	Tool Shed	1		1	1										
87				General Requirements	Tool Shed	1		1	1										
88				General Requirements	Tool Shed	1		1	1										
89				General Requirements	Tool Shed	1		1	1										
90				General Requirements	Tool Shed	1		1	1										
91				General Requirements	Tool Shed	1		1	1										
92				General Requirements	Tool Shed	1		1	1										
93				General Requirements	Tool Shed	1		1	1										
94				General Requirements	Tool Shed	1		1	1										
95				General Requirements	Tool Shed	1		1	1										
96				General Requirements	Tool Shed	1		1	1										
97				General Requirements	Tool Shed	1		1	1										
98				General Requirements	Tool Shed	1		1	1										
99				General Requirements	Tool Shed	1		1	1										

TOTAL LABOR COST		TOTAL MATERIAL COST		TOTAL MATERIAL COST		ITEM COST		TRADE COST		UNIT-ITEM COST WITH MARKUPS		TOTAL ITEM COST WITH MARKUPS	
HOURS	PER HOUR LABOR RATE	TOTAL LABOR COST	PER HOUR MATERIAL COST	TOTAL MATERIAL COST	ITEM COST	TRADE COST	UNIT-ITEM COST WITH MARKUPS	TOTAL ITEM COST WITH MARKUPS					
428.22	78.00	33,408.24	1,956.00	176,046.00	206,448		2,724.50	245,293					
28.55	78.00	2,222.22	1,956.00	11,786.00	13,963		2,724.50	16,946					
12.72	78.00	992.40	298.50	1,419.30	2,613		463.98	2,784					
74.80	78.00	5,833.60	854.00	12,934.00	23,700		1,318.80	27,693					
3.56	78.00	277.08	854.00	854.00	1,332		1,318.80	1,318					
4.76	78.00	372.24	2,998.00	2,998.00	2,227		2,724.50	2,724					
86.54	78.00	6,753.60	1,538.00	24,314.40	31,104		1,728.40	36,297					
13.96	78.00	1,084.90	240.00	1,440.00	2,484		477.07	2,886					
25.00	78.00	1,956.00	260.00	2,880.00	4,817		505.60	5,382					
71.90	78.00	5,609.70	95.00	7,880.00	13,560		186.70	15,687					
120.40	78.00	9,391.20	49,317.40	98,634.80	106,028		63,465.25	126,973					
402.50	78.00	31,395.00	95,010.00	475,097.80	516,400		120,096.62	605,483					
11.00	78.00	858.20	57.50	575.10	1,433		183.73	1,637					
32.50	78.00	2,535.00	34,131.50	34,131.50	36,667		48,138.97	81,130					
13.50	78.00	1,053.20	2,300.00	3,600.00	4,653		1,269.12	5,427					
13.50	78.00	1,053.20	5,260.00	15,780.00	16,833		6,191.98	18,736					
3.75	78.00	292.40	375.00	1,125.00	1,431		551.74	1,551					
2.25	78.00	175.50	95.00	285.00	468		177.12	638					
9.00	78.00	702.00	1,200.00	3,780.00	2,487		2,252.34	5,184					
4.50	78.00	351.00	490.00	1,360.00	1,700		662.00	1,960					
9.60	78.00	748.80	2,100.00	6,360.00	7,100		2,782.80	8,347					
0.60	78.00	46.80	8.50	53.00	98		78.75	127					
32.00	78.00	2,496.00	4,800.00	19,400.00	21,887		6,424.40	25,686					
16.00	78.00	1,248.00	1,500.00	10,300.00	11,507		6,778.70	13,513					
10.50	78.00	819.00	758.60	2,78.50	3,095		1,200.90	3,693					
1.50	78.00	117.00	126.00	256.00	367		237.85	428					
1.25	78.00	97.50	285.00	285.00	383		385.97	487					
1.00	78.00	78.00	180.00	180.00	240		135.34	218					
1.00	78.00	78.00	85.00	130.00	248		143.92	227					
48.00	78.00	3,744.00	85.00	3,860.00	5,800		108.89	5,909					
96.00	78.00	7,488.00	98.00	8,800.00	12,800		186.66	12,886					
120.00	78.00	9,360.00	53.00	5,300.00	14,563		186.66	14,649					
2,048.50	78.00	159,820.40	2.70	46,514.20	208,339		53,123.00	211,737					
431.75	78.00	33,666.60	0.20	26,124.20	59,790		1,897.00	60,687					
2,312.15</													



ITEM #	REF. SHEET	DETAIL	CS. SECT.	Sub Contractor	DESCRIPTION	QTY.	WASTAGE	QTY WITH WASTAGE	UNIT	UNIT LABOR HOURS	TOTAL LABOR HOURS	PER HOUR LABOR RATE	TOTAL LABOR COST	UNIT MATERIAL COST	TOTAL MATERIAL COST	ITEM COST	TRADE COST	UNIT ITEM COST WITH MARKUPS	TOTAL ITEM COST WITH MARKUPS
404	C412 - C442		DOV-32	Erosion Control	Construction Fence	(146)	5%	153	LF	0.250	(38.815)	61.50	2,388.00	2.50	380.40	2,768.40		20.30	1,120
405	C412 - C442		DOV-32	Erosion Control	12" HDPE Temporary Drainage Connection	(1)	5%	1	LF	0.000	(0.000)	61.50	0.00	0.00	0.00	0.00		0.00	0.00
406	C412 - C442		DOV-32	Erosion Control	12" HDPE Temporary Drainage Connection	(130)	5%	137	LF	0.500	(68.150)	61.50	4,193.00	13.80	2,448.30	6,641.30		50.30	7,290
407	C412 - C442		DOV-32	Erosion Control	12" HDPE Temporary Drainage Connection	(1)	5%	1	LF	0.000	(0.000)	61.50	0.00	0.00	0.00	0.00		0.00	0.00
408	C412 - C442	Specs		Erosion Control	Erosion Control Barrier (Biodegradable Wood Fackelbar, Stray Or Coconut-Fiber Mat, Enclosed in a Photodegradable Plastic Mesh)	(47,835)	5%	50,222	SF	0.012	(602.725)	61.50	37,602.80	1.90	95,910.60	129,942.40		8.60	438,444
PAVE																			
409	L305	L305	DOV-32	Fencing and Gates - Wood	4" High Decore Aluminum Fence and Gate W/ 8" O.C. Post	(161)	5%	169	LF	1.250	(211.31)	79.61	16,825.81	28.51	4,617.91	21,643.71		144.70	24,472
410	L305	2-LS04C	DOV-32	Fencing and Gates - Wood	8" Post Screen Fence W/ 3/8"x12 Ga. Post 8" O.C. Interlocks	(306)	5%	321	LF	1.500	(481.95)	79.61	38,874.81	42.81	13,735.51	52,110.31		183.81	58,060
411	L305	2-LS04C	DOV-32	Fencing and Gates - Wood	8" Ornamental Iron Fence W/ 3/8"x12 Ga. Post 8" O.C. Terminal Panels	(113)	5%	119	LF	1.750	(207.64)	79.61	16,532.71	65.31	7,741.91	24,374.61		212.61	27,003
412	L305	3-LS03	DOV-32	Fencing and Gates - Wood	1.75" Fabric Diamond Mesh Interlocks 6 Gauge Wire Knuckled salvage Top & Bottom Black PVC Coated, Fuse Bonded	2488.26	5%	2,613	LF	0.750	(1,959.50)	79.61	154,021.61	13.81	36,834.1	188,855.6		81.97	214,255
413	L305	3-LS03	DOV-32	Fencing and Gates - Wood	1.25" Fabric Diamond Mesh Interlocks 6 Gauge Wire Knuckled salvage Top & Bottom Black PVC Coated, Fuse Bonded	4800	5%	5,144	LF	0.850	(4,372.81)	79.61	348,142.21	15.31	78,445.2	426,587.3		95.57	481,339
414	L305	3-LS03	DOV-32	Fencing and Gates - Wood	1.68" Diameter Top and Bottom Rail 2" x 2" Diameter Line Post 10" O.C. 8" High Chain Link Fence W/ 1.75" Fabric Diamond Mesh Interlocks 6 Gauge Wire Knuckled salvage	375	5%	394	LF	1.100	(433.13)	79.61	34,486.71	18.81	7,362.81	41,849.5		110.93	47,223
415	L305	3-LS03	DOV-32	Fencing and Gates - Wood	1.68" Diameter Top and Bottom Rail 2" x 2" Diameter Line Post 10" O.C. 8" High Chain Link Fence W/ 1.75" Fabric Diamond Mesh Interlocks 6 Gauge Wire Knuckled salvage	1100	5%	1,153	LF	1.100	(1,273.50)	79.61	117,846.81	24.51	28,297.5	146,144.3		162.28	187,483
416	L305	3-LS03	DOV-32	Fencing and Gates - Wood	1.68" Diameter Top and Bottom Rail 2" x 2" Diameter Line Post 10" O.C. 8" High Chain Link Fence W/ 1.75" Fabric Diamond Mesh Interlocks 6 Gauge Wire Knuckled salvage	86	5%	90	LF	1.250	(383.78)	79.61	35,557.51	85.01	7,275.51	38,233.0		478.20	43,881
417	L305	3-LS03	DOV-32	Fencing and Gates - Wood	1.68" Diameter Top and Bottom Rail 2" x 2" Diameter Line Post 10" O.C. 8" High Chain Link Fence W/ 1.75" Fabric Diamond Mesh Interlocks 6 Gauge Wire Knuckled salvage	80	5%	84	LF	1.500	(294.00)	79.61	21,420.01	72.51	6,090.01	29,490.0		196.77	31,328
IRRIGATION																			
418			DOV-32	Landscape	Sprays / Impact Irrigation Area	(206,179)	5%	206,513	SF	0.012	(2,478.16)	62.31	154,295.21	1.01	208,578.5	362,874		2.03	418,562
LANDSCAPING																			
419			DOV-	Landscape	Reinstall Grass Sodded Lawn	(16,474)	5%	16,499	SF	0.004	(389.76)	62.31	24,018.61	1.51	145,623.6	169,641		2.00	158,767
420			DOV-	Landscape	8" Top Soil	(16,474)	5%	16,499	SF	0.042	(4,098.40)	62.31	252,180.5	1.21	15,727.2	367,877		8.30	371,287
421			DOV-	Landscape	12" Washed Sand	(16,474)	5%	16,499	SF	0.058	(2,571.72)	62.31	162,102.5	0.21	560,431.6	723,027		9.71	812,249
PLANT EVERGREENS AND BALSAM																			
422	AE105	AE105	DOV-32	Landscape	Tag 1N, Botanical Name: Thuja occidentalis 'Nigra', Common Name: Bush Arborvitae, Root: B&S, Size: 6-8" HT, 1-4" DB	(10)	(10)	EA	2.320	(23.20)	62.31	1,444.51	90.01	3,500.01	4,944		174.61	5,740	
423	AE105	AE105	DOV-32	Landscape	Tag 1S, Botanical Name: Thuja occidentalis 'Smaragd', Common Name: General Green Arborvitae, Root: B&S, Size: 6-8" HT, 1-4" DB	(21)	(21)	EA	2.320	(48.72)	62.31	3,033.41	90.01	7,510.01	10,383		174.61	12,087	
ORNAMENTAL																			
424	AE101	AE101	DOV-32	Landscape	Tag AG, Botanical Name: Amelanchier x grandiflora 'Autumn Brilliance', Common Name: Autumn Brilliance Apple Serviceberry, Root: B&S, Size: 10-12" HT, 1-2" DB	(4)	(4)	EA	1.254	(13.02)	62.31	820.41	600.01	2,400.01	3,210		974.70	3,700	
SHRUBS																			
425	AE101	AE101	DOV-32	Landscape	Tag TR, Botanical Name: Thuja americana 'Redmond', Common Name: Redmond American Linden, Root: B&S, Size: 10-12" HT, 1-2" DB	(3)	(3)	EA	3.865	(11.60)	62.31	721.81	90.01	2,650.01	3,572		1,190.58	4,722	
EVERGREEN SHRUBS																			
426	AE101	AE101	DOV-32	Landscape	Tag RB, Botanical Name: Juniperus squarata 'Blue Star', Common Name: Blue Star Juniper, Root: #3 CONT., Size: 15-18" HT, 12-15" SP	(69)	(69)	EA	0.457	(31.50)	62.31	1,961.21	55.01	3,795.01	5,746		96.60	6,071	
427	AE101	AE101	DOV-32	Landscape	Tag RB, Botanical Name: Juniperus conferta 'Blue Pacific', Common Name: Blue Pacific Shrub Juniper, Root: #3 CONT., Size: 15-18" HT, 12-15" SP	(23)	(23)	EA	0.498	(12.41)	62.31	779.21	60.01	1,500.01	2,279		105.40	2,687	
428	AE101	AE101	DOV-32	Landscape	Tag JT, Botanical Name: Juniperus chinensis 'Sea Green', Common Name: Sea Green Juniper, Root: #3 CONT., Size: 15-18" HT, 12-15" SP	(57)	(57)	EA	0.457	(26.02)	62.31	1,630.11	55.01	3,119.01	4,750		96.60	5,511	
429	AE101	AE101	DOV-32	Landscape	Tag JPS, Botanical Name: Juniperus rigida conferta 'MGSF', Common Name: MGSF Juniper, Root: #3 CONT., Size: 15-18" HT, 12-15" SP	(16)	(16)	EA	0.398	(6.37)	62.31	396.81	48.01	768.01	1,165		84.30	1,350	
430	AE101	AE101	DOV-32	Landscape	Tag JS, Botanical Name: Juniperus chinensis 'Turfgold', Common Name: Turfgold Juniper, Root: #3 CONT., Size: 15-18" HT, 12-15" SP	(23)	(23)	EA	0.457	(10.50)	62.31	653.71	55.01	1,260.01	1,919		96.60	2,244	
431	AE101	AE101	DOV-32	Landscape	Tag JS, Botanical Name: Juniperus chinensis 'Blue Star', Common Name: Blue Star Juniper, Root: #3 CONT., Size: 15-18" HT, 12-15" SP	(66)	(66)	EA	0.457	(30.33)	62.31	1,875.91	55.01	3,600.01	5,506		96.60	6,363	
GROUND COVERS																			
432	AE101	AE101	DOV-32	Landscape	Tag HPS, Botanical Name: Hemerocallis 'Happy Returns', Common Name: Happy Returns Daylily, Root: #3 CONT., Size: Not specified	(243)	(243)	EA	0.250	(60.75)	62.31	3,762.41	42.01	4,374.01	8,156		38.64	9,389	
SH-35																			
Geothermal Bore Field System																			
Geothermal Bore																			
433	MSU100	MSU101	DOV-33	Mechanical	12" Dia. 900' Bore Well	(182)	5%	191	EA	8.000	(2,040.00)	98.51	200,890.4		- \$5	200,890		879.89	214,371
Geothermal Bore																			
434	MSU100	MSU101	DOV-	Mechanical	12" Dia. 900' Bore Well	(182)	5%	191	EA	0.256	(36.36)	98.51	1,564.81	7.71	1,093.01	4,678		37.24	1,730
435	MSU100	MSU101	DOV-	Mechanical	12" Dia. 900' Bore Well	(182)	5%	191	EA	0.256	(36.36)	98.51	1,564.81	7.71	1,093.01	4,678		37.24	1,730
436	MSU100	MSU101	DOV-	Mechanical	12" Dia. 900' Bore Well	(182)	5%	191	EA	0.256	(36.36)	98.51	1,564.81	7.71	1,093.01	4,678		37.24	1,730
437	MSU100	MSU101	DOV-	Mechanical	12" Dia. 900' Bore Well	(182)	5%	191	EA	0.256	(36.36)	98.51	1,564.81	7.71	1,093.01	4,678		37.24	1,730
438	MSU100	MSU101	DOV-	Mechanical	12" Dia. 900' Bore Well	(182)	5%	191	EA	0.256	(36.36)	98.51	1,564.81	7.71	1,093.01	4,678		37.24	1,730
439	MSU100	MSU101	DOV-	Mechanical	12" Dia. 900' Bore Well	(182)	5%	191	EA	0.256	(36.36)	98.51	1,564.81	7.71	1,093.01	4,678		37.24	1,730
440	MSU100	MSU101	DOV-	Mechanical	12" Dia. 900' Bore Well	(182)	5%	191	EA	0.256	(36.36)	98.51	1,564.81	7.71	1,093.01	4,678		37.24	1,730
441	MSU100	MSU101	DOV-	Mechanical	12" Dia. 900' Bore Well	(182)	5%	191	EA	0.256	(36.36)	98.51	1,564.81	7.71	1,093.01	4,678		37.24	1,730
442	MSU100	MSU101	DOV-	Mechanical	12" Dia. 900' Bore Well	(182)	5%	191	EA	0.256	(36.36)	98.51	1,564.81	7.71	1,093.01	4,678		37.24	1,730
443	MSU100	MSU101	DOV-	Mechanical	12" Dia. 900' Bore Well	(182)	5%	191	EA	0.256	(36.36)	98.51	1,564.81	7.71	1,093.01	4,678		37.24	1,730
Water Pipe Material to HDPE																			
444	MSU100	MSU101	DOV-33	Mechanical	12" Dia. 900' Bore Well	(182)	5%	191	EA	0.256	(36.36)	98.51	1,564.81	7.71	1,093.01	4,678		37.24	1,730
445	MSU100	MSU101	DOV-	Mechanical	12" Dia. 900' Bore Well	(182)	5%	191	EA	0.256	(36.36)	98.51	1,564.81	7.71	1,093.01	4,678		37.24	1,730
446	MSU100	MSU101	DOV-	Mechanical	12" Dia. 900' Bore Well	(182)	5%	191	EA	0.256	(36.36)	98.51	1,564.81	7.71	1,093.01	4,678		37.24	1,730
447	MSU100	MSU101	DOV-	Mechanical	12" Dia. 900' Bore Well	(182)	5%	191	EA	0.256	(36.36)	98.51	1,564.81	7.71	1,093.01	4,678		37.24	1,730
448	MSU100	MSU101	DOV-	Mechanical	12" Dia. 900' Bore Well	(182)	5%	191	EA	0.256	(36.36)	98.51	1,564.81	7.71	1,093.01	4,678		37.24	1,730
449	MSU100	MSU101	DOV-	Mechanical	12" Dia. 900' Bore Well	(182)	5%	191	EA	0.256	(36.36)	98.51	1,564.81	7.71	1,093.01	4,678		37.24	1,730
450	MSU100	MSU101	DOV-	Mechanical	12" Dia. 900' Bore Well	(182)	5%	191	EA	0.256	(36.36)	98.51	1,564.81	7.71	1,093.01	4,678		37.24	1,730
451	MSU100	MSU101	DOV-	Mechanical	12" Dia. 900' Bore Well	(182)	5%	191	EA	0.256	(36.36)	98.51	1,564.81	7.71	1,093.01	4,678		37.24	1,730
452	MSU100	MSU101	DOV-	Mechanical	12" Dia. 900' Bore Well	(182)	5%	191	EA	0.256	(36.36)	98.51	1,564.81	7.71	1,093.01	4,678		37.24	1,730
453	MSU100	MSU101	DOV-	Mechanical	12" Dia. 900' Bore Well	(182)	5%	191	EA	0.256	(36.36)	98.51	1,564.81	7.71	1,093.01	4,678		37.24	1,730
454	MSU100	MSU101	DOV-	Mechanical	12" Dia. 900' Bore Well	(182)	5%	191	EA	0.256	(36.36)	98.51	1,564.81	7.71	1,093.01	4,678		37.24	1,730
455	MSU100	MSU101	DOV-	Mechanical	12" Dia. 900' Bore Well	(182)	5%	191	EA	0.256	(36.36)	98.51	1,564.81	7.71	1,093.01	4,678		37.24	1,730
456	MSU100	MSU101	DOV-	Mechanical	12" Dia. 900' Bore Well	(182)	5%	191	EA	0.256	(36.36)	98.51	1,564.81	7.71	1,093.01	4,678		37.24	1,730
457	MSU100	MSU101	DOV-	Mechanical	12" Dia. 900' Bore Well	(182)	5%	191	EA	0.256	(36.36)	98.51	1,564.81	7.71	1,093.01	4,678		37.24	1,730
458	MSU100	MSU101	DOV-	Mechanical	12" Dia. 900' Bore Well	(182)	5%	191	EA	0.256	(36.36)	98.51	1,						

Note: Adjusting the per hour labor rate in the table below will automatically update the labor pricing for whole project. To bypass the per hour labor rate for a single item, please put the per hour labor rate against that item in column M of relative tab.

[CLICK HERE TO GO BACK TO COST SUMMARY](#)

CSI Div.	Sub-Contractor/Trade List	Hourly Rates
DIV-1	General Requirements	(\$ 66.11)
DIV-10	Accessories	(\$ 79.62)
DIV-09	Acoustical and Metal Ceiling	(\$ 82.94)
DIV-11	Appliances	(\$ 83.79)
DIV-02	Asbestos Worker	(\$ 85.23)
DIV-10	Awnings / Canopies	(\$ 86.04)
DIV-12	Cabinetry	(\$ 79.62)
DIV-06	Carpenter Millwork	(\$ 79.62)
DIV-09	Ceiling - Others	(\$ 82.94)
DIV-07	Cladding - Metal	(\$ 92.19)
DIV-06	Cladding - Wood	(\$ 78.92)
DIV-06	Cladding - Other	(\$ 85.56)
DIV-09	Clean - Power Wash	(\$ 64.69)
DIV-31	Clearing & Grubbing	(\$ 148.69)
DIV-27	Communication	(\$ 81.00)
DIV-03	Concrete - Building	(\$ 68.30)
DIV-12	Countertops	(\$ 71.54)
DIV-08	Curtain Wall	(\$ 71.50)
DIV-02	Demo - Building	(\$ 62.00)
DIV-02	Demo - Site	(\$ 62.00)
DIV-31	Dewatering	(\$ 148.69)
DIV-08	Doors & Hardware	(\$ 80.12)
DIV-09	Dry Waller	(\$ 82.94)
DIV-31	Earth worker	(\$ 115.23)
DIV-26	Electrician	(\$ 81.00)
DIV-28	Electronic Safety and Security (FA)	(\$ 81.00)
DIV-14	Elevator	(\$ 130.26)
DIV-11	Equipment	(\$ 86.72)
DIV-31	Erosion Control	(\$ 61.49)
DIV-32	Exterior Improvements	(\$ 68.30)
DIV-09	Exterior Painter	(\$ 86.78)
DIV-10	Exterior Signage	(\$ 79.62)
DIV-32	Fencing and Gates - Metal	(\$ 85.89)
DIV-32	Fencing and Gates - Wood	(\$ 79.62)
DIV-32	Fencing and Gates - Other	(\$ 82.76)
DIV-06	Finish Carpenter	(\$ 79.62)
DIV-09	Fire Proofing	(\$ 65.27)
DIV-21	Fire Suppression	(\$ 104.04)
DIV-10	Fireplace	(\$ 58.23)
DIV-09	Flooring	(\$ 78.14)
DIV-10	Folding/Moveable Partition	(\$ 80.12)
DIV-05	Framer Cold Form	(\$ 82.94)
DIV-09	Framer Light Gauge	(\$ 82.94)
DIV-06	Framer Lumber	(\$ 82.94)
DIV-06	Framer Rough Carpenter	(\$ 82.94)
DIV-12	Furniture	(\$ 64.17)
DIV-08	Glazier	(\$ 82.00)
DIV-02	Hazardous Material Handler	(\$ 85.23)
DIV-07	Insulation	(\$ 82.94)
DIV-09	Interior Painter	(\$ 86.78)
DIV-10	Interior Signage	(\$ 79.62)
DIV-32	Irrigation	(\$ 62.26)
DIV-07	Joint Sealants	(\$ 69.73)
DIV-32	Landscape	(\$ 62.26)
DIV-12	Mailboxes	(\$ 79.62)
DIV-04	Mason - Brick Veneer	(\$ 80.78)
DIV-04	Mason - Cast Stone	(\$ 83.11)
DIV-04	Mason - CMU	(\$ 77.15)
DIV-23	Mechanical	(\$ 98.51)
DIV-06	Millwork	(\$ 79.62)
DIV-05	Ornamental Steel	(\$ 86.04)
DIV-05	Paneling - Metal	(\$ 92.19)
DIV-06	Paneling - Wood	(\$ 79.62)
DIV-06	Paneling - Other	(\$ 85.90)
DIV-32	Paving	(\$ 68.30)
DIV-06	Pergolas	(\$ 82.53)
DIV-31	Piling	(\$ 120.77)
DIV-11	Playground Equipment	(\$ 66.45)
DIV-22	Plumber	(\$ 87.90)
DIV-13	Pool	(\$ 90.17)
DIV-03	Precast Concrete	(\$ 68.30)
DIV-13	Pre-Engineered Metal Building	(\$ 144.86)
DIV-06	Roof Sheathing	(\$ 82.94)
DIV-07	Roofer	(\$ 78.57)
DIV-06	Sheathing	(\$ 82.94)
DIV-31	Shoring/SOE	(\$ 82.36)

DIV-07	Siding Contractor	(\$ 85.17)
DIV-03	Site Concrete	(\$ 81.10)
DIV-26	Site Electrical	(\$ 78.02)
DIV-12	Site Furnishing	(\$ 79.62)
DIV-09	Site Paint	(\$ 86.78)
DIV-10	Site Signage	(\$ 79.62)
DIV-08	Skylight	(\$ 79.62)
DIV-13	Special Construction	(\$ 86.04)
DIV-05	Staircases and Railings - Metal	(\$ 86.04)
DIV-06	Staircases and Railings - Wood	(\$ 79.62)
DIV-08	Storefront	(\$ 67.16)
DIV-05	Structural Steel	(\$ 68.00)
DIV-07	Stucco - EIFS	(\$ 70.34)
DIV-09	Tiler	(\$ 81.39)
DIV-10	Toilet Partitions	(\$ 79.62)
DIV-34	Traffic Control	(\$ 82.94)
DIV-06	Trellis	(\$ 79.85)
DIV-06	Truss	(\$ 68.54)
DIV-33	Utilities	(\$ 82.36)
DIV-09	Wall Covering	(\$ 86.78)
DIV-07	Water Proofing & Damp Proofing	(\$ 77.15)
DIV-08	Window Installer	(\$ 79.62)
DIV-10	Wire Shelving	(\$ 79.62)
DIV-00	Z	
DIV-01	Z	

Unit	Wastage
EA	0%
LF	5%
SF	5%
SY	5%
LBS	5%
TONS	5%
CY	5%
LS	0%

[illegible]

Project Dashboard

Project Name

Date

Base Bid

Project type



Address

Scope of Work

Overall Estimate

Basebid

Add ALT

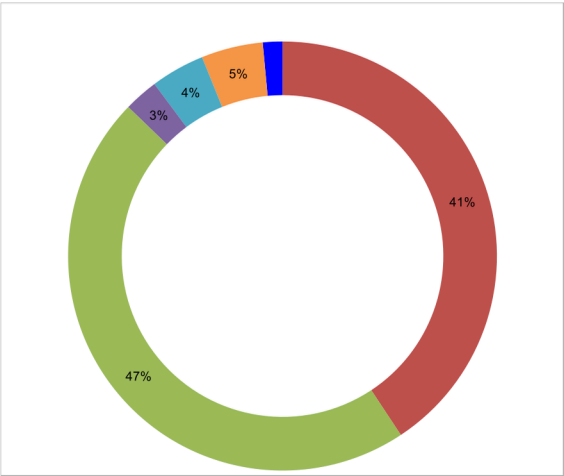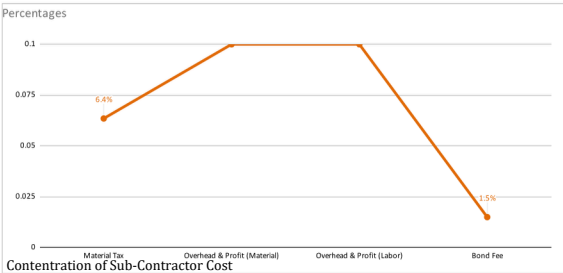

Cost Summary

